

INSTALLATION REPORT

DataMaster DMT: 100156
Location: Castleton VSP
Calibration Date: 11/03/2011
Certification Date: 11/03/2011
Installation Date: 12/01/2011
Installed by: STEVEN E HARNOIS



Site meets specification in doc P-ALC-210

Result Options Loaded

Diagnostic Results

VERSIONS

DMT: 1.01
PIC: 2.05
Modem: 2.2
Questions: 2.0

TEMPERATURES

Sample Chamber = 48.9°C
Breath Tube = 47.3°C
Digital Sim = 34.0°C

SETTINGS

Lamp Voltage = 1.83 V
Cooler Voltage = 1.79 V
Bias Voltage = 80 V
Chopper Freq = 537 Hz

PUMP INFO

Flow Rate = 5.746 L/M

DETECTOR INFO

PUMP	ON	OFF
MAX (V)	0.0770	0.0823
MIN (V)	0.0756	0.0809

FILTER INFO

Filter	Value	Zero
Filter 1	0.081	true
Filter 2	0.205	true
Filter 3	1.135	true

CALIBRATION CHECK

Xq = 0.096 0.27%

Accuracy and Precision Check


Concentration	= 0.100 g/210L
Lot #	= 12-32-100
Range	= 0.095 - 0.105
Average	= 0.101 g/210L
Std Dev	= 0.0000

RF Detection Test

Passed

Sample Acceptance Test

Passed

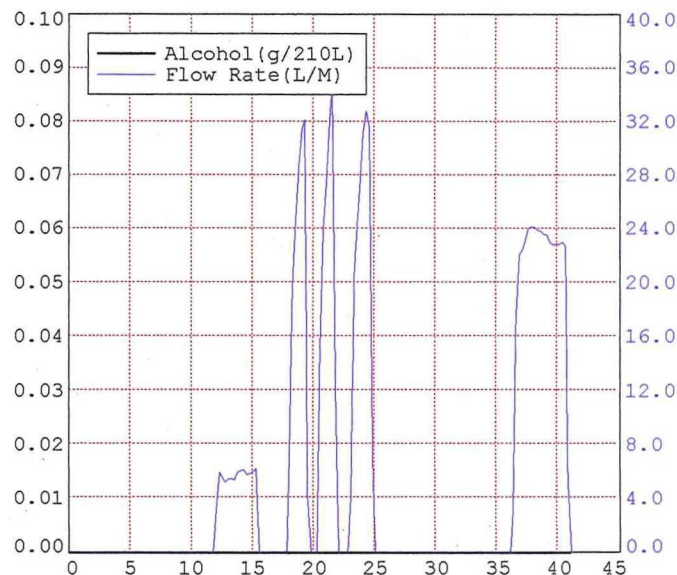

INSTALLATION PASSED

Performed by

[Signature]

Date

12/01/2011

Reviewed by

[Signature]

Date

12-1-11
