



Bennington Bridge #6 Public Presentation

Bennington BF 1000(20)

March 11, 2026

Project Team

Rob Young, P.E.

VTrans
Project Manager

Tom Knight, P.E.

Stantec
Design Consultant

Leah Beckett

IMEG
Public Information Consultant

Mark Mackintosh, P.E.

VTrans / GPI
Resident Engineer

Phil Romero

Kubricky Jointa Lime
Contractor

Cale Gleason

Kubricky Jointa Lime
Contractor

Location Map




Agenda

- Project History
- Project Overview
- Construction Schedule
- Traffic Impacts/Detours
- Public Outreach
- Questions

Bridge 6 Project History

- Located in Downtown Bennington
- Originally constructed in 1923
- Reinforced concrete T-beam structure

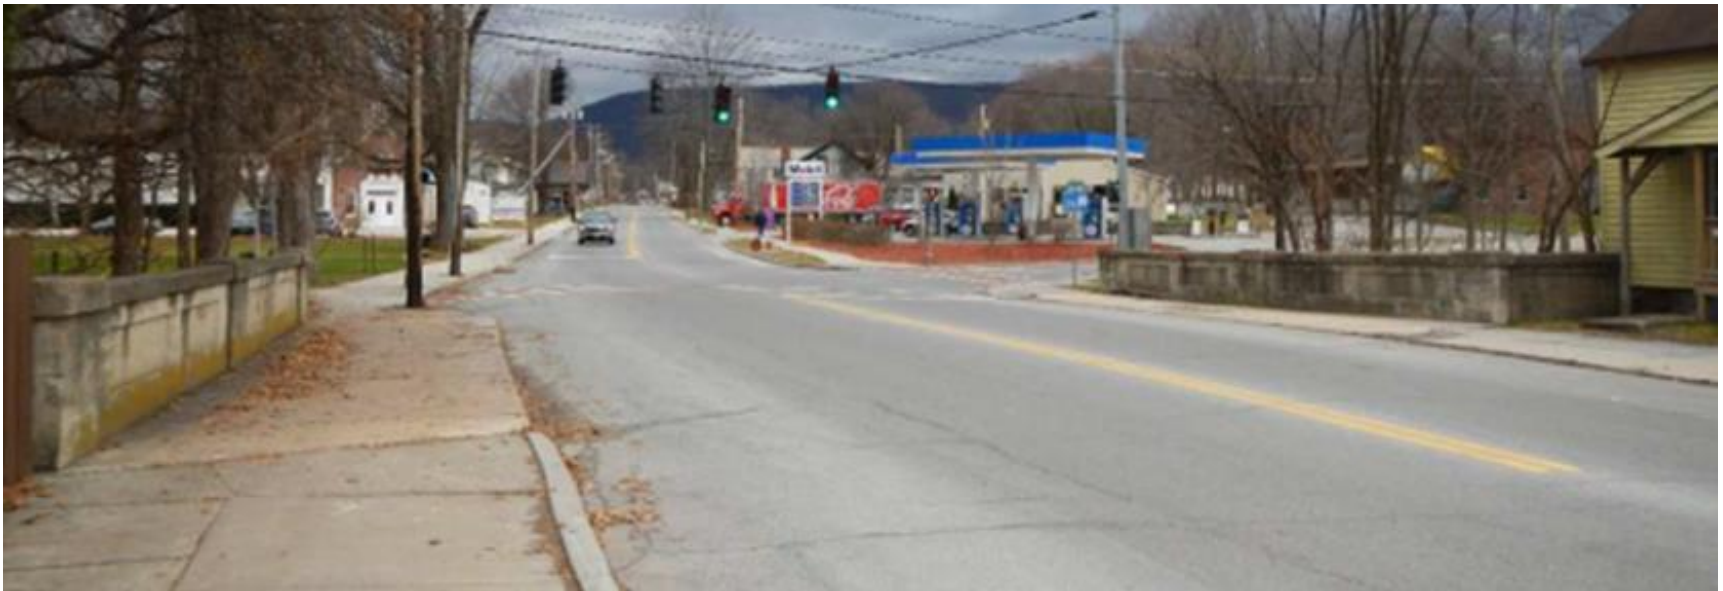

Project Overview – Existing Conditions

- Deck, superstructure, and substructure are currently rated “Fair”
- Visible concrete deterioration and drainage-related damage
- Undersized for larger storm events



Project Overview

- Full bridge replacement on existing alignment
- Designed for a 75+ year design life
- Maintains existing roadway width and sidewalks



How the New Bridge Will Be Built



Adjacent deck beams placed side by side



Prefabricated element construction placed by crane

- Bridge components fabricated off-site
- Delivered and lifted into place
- **Faster installation with less disruption**

Allows the bridge to be installed faster and **reduces road closure time**

Construction Schedule



2025

- Relocation of Private Utilities
- Lining and Reinforcement of Municipal Sewer
- Temporary Relocation of Municipal Water
- Drainage Installation
- Pile Installation

Construction Schedule



2026

- Weather permitting, work begins March 23 with lane closures.
- **Full bridge closure is anticipated from April 13 to early June.**
 - *Night work is expected during the initial demolition and closure period.*
- During the summer, daily single lane closures with flaggers or temporary signals will be in effect.
- Overall project completion is expected in late August.

Traffic Detours

- **Passenger Vehicles, Pedestrians, and Cyclists:**

- Safford - Gage - Bradford

- **Trucks:**

- VT 9 - US 7 - VT 279

**Anticipated Bridge
Closure Period is from
April 13 to Early June**



Local & Pedestrian Detour

- **Passenger vehicles, pedestrians, and cyclists should follow the marked signs on:**
 - Safford - Gage - Bradford

Anticipated Bridge Closure Period is from April 13 to Early June




State Route Detour

- **Trucks:**

- VT 9 - US 7 - VT 279

**Anticipated Bridge
Closure Period is from
April 13 to Early June**

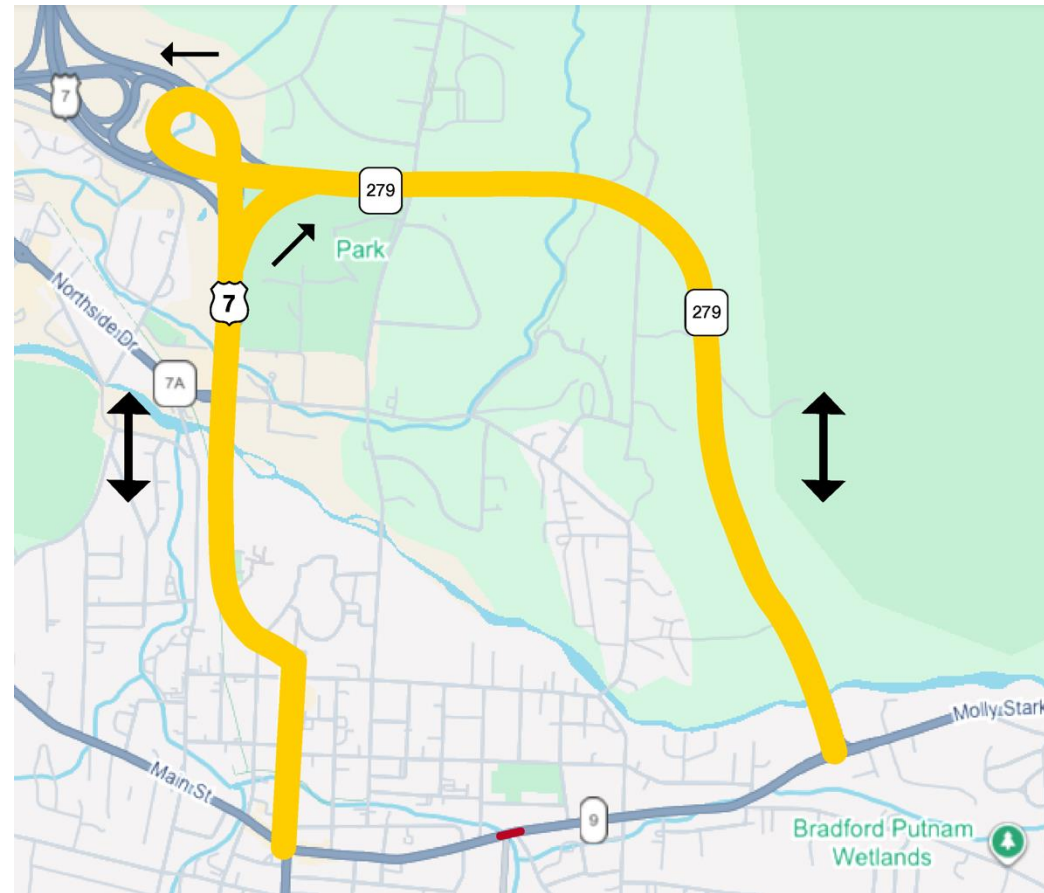

Thank you!

QUESTIONS?
