

2022 School Facilities Inventory Report

Facility Name: **HARTFORD SD | HARTFORD HIGH SCHOOL | 37 HIGHLAND AVENUE, WHITE RIVER JCT 5001 - High (9 thru 12) - Main Building**


March 29, 2022

Total Value of Assets (Does Not Include Site/Structure/Walls/Interiors) **\$10,250,453**



GPS: 43.65724673976165, -72.32053750646817

Relative Asset Values


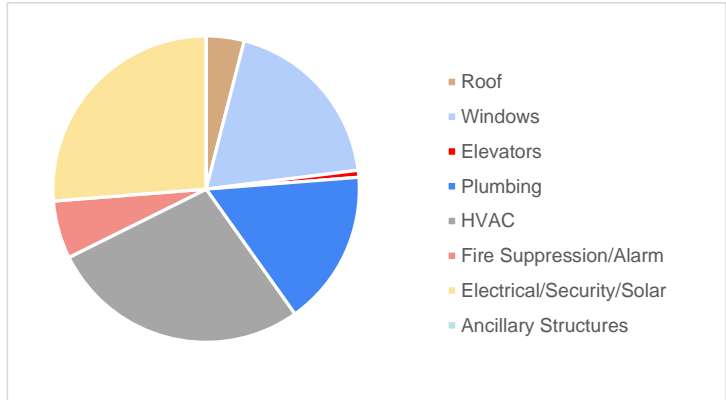


Value of Assets/GSF **\$91.47**




Site Plan - Google Earth

Projected Capital Planning Cash Flow

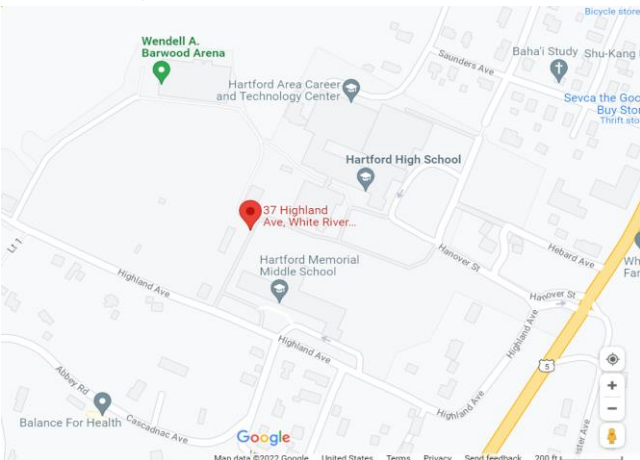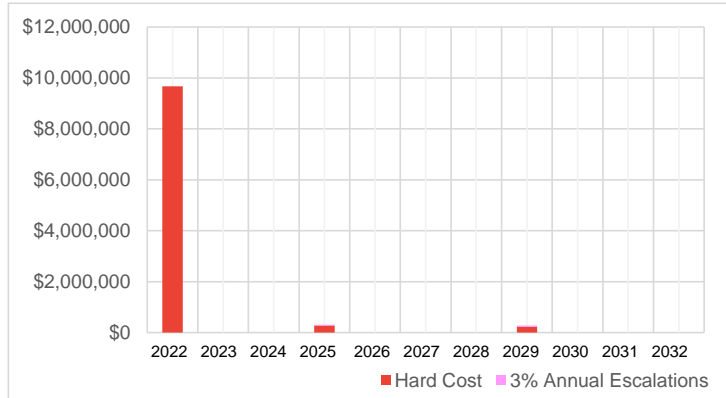

Location Plan - Google Maps

Facility Condition Index (FCI) Compared to Portfolio

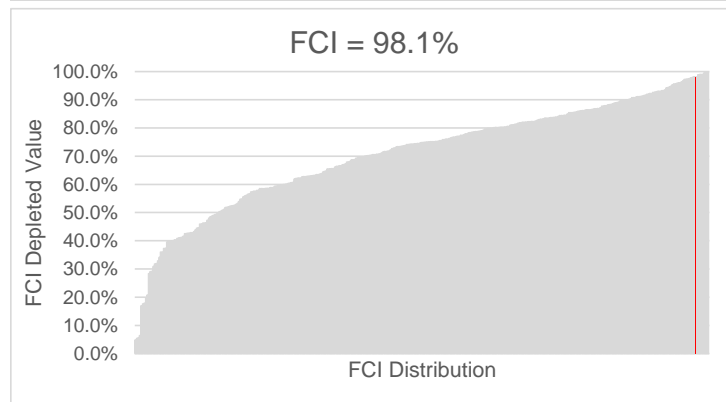

(See Last Page for Explanation of Terms)

2022 School Facilities Inventory Report

Facility Name: **HARTFORD SD | HARTFORD HIGH SCHOOL | 37 HIGHLAND AVENUE, WHITE RIVER JCT 5001 - High (9 thru 12) - Main Building**

Respondent Information

Date/Time Completed **2022-01-19 - 2:15 PM**
 Respondent Name **JONathan Garthwaite**
 Respondent Title **Director of Buildings and Grounds**
 Respondent Email **garthwaitej@hartfordschools.net**
 Respondent Phone Number **(802) 359-4610**

Facility Information

School Type **High (9 thru 12)**
 Building Identification **Main Building**
 Stories **3**
 Building Area **112066 (Gross Square Footage - GSF)**
 Year Constructed **1964**
 Year of Last Major Renovation **N/A**
 FCI (Depleted Value) **98.1%**

Environmental & Safety Issues

Hazardous Materials **Yes** ⚠
 Hazardous (HZD) Materials include **Asbestos containing materials (ACM)**
 HZD Issues are **Minor**
 HZD Issues include **Suspect ACM from construction**

Indoor Air Quality (IAQ) Issues **No**
 IAQ Issues include **-**
 IAQ Issues are **-**
 IAQ Issues include **-**

Fire or Life/Safety (FL/S) Issues **Yes** ⚠
 FL/S Issues are **Fire alarm System needs to be replaced. Building not fully sprinklered.**

Other Risk Factors **No**
 Other Risk Factors include **-**
 Other Risk Factors are **-**

Handicap Accessibility (ADA) Issues

Handicap Accessibility (ADA) Issues **No**
 ADA Issues are **N/A**
 ADA Issues include **N/A**

Utilities - Adequacy

IT / Internet Service **Adequate**
 Building Wi-Fi Coverage **Adequate**
 Cellular Reception **Adequate**
 Water Service Pressure **Adequate**
 Natural Gas/Propane Pressure **Adequate**
 Electrical Capacity **Adequate**

2022 School Facilities Inventory Report

Facility Name: **HARTFORD SD | HARTFORD HIGH SCHOOL | 37 HIGHLAND AVENUE, WHITE RIVER JCT 5001 - High (9 thru 12) - Main Building**

Building Envelope - Roof

Roof 1 is	Single-Ply EPDM/TPO/PVC Membrane								
Covers	100%	EUL	C-RUL	Cost / Unit		Quantity	Units	=	Total Value
Installed in	1986	20	-16	\$11.00 / SF	for	37,355 SF			\$410,909
Roof 2 is	-								
Covers	0%	EUL	C-RUL	Cost / Unit		Quantity	Units	=	Total Value
Installed in	-	-	N/A	- / -	for	-	-		\$0
Roof 3 is	-								
Covers	0%	EUL	C-RUL	Cost / Unit		Quantity	Units	=	Total Value
Installed in	-	-	N/A	- / -	for	-	-		\$0
Roof 4 is	-								
Covers	0%	EUL	C-RUL	Cost / Unit		Quantity	Units	=	Total Value
Installed in	-	-	N/A	- / -	for	-	-		\$0



Building Envelope - Windows

Primary Window System	Window, Metal-Frame								
% of Windows That are this Type	75%	EUL	C-RUL	Cost / Unit		Quantity	Units	=	Total Value
Installed in	1964	30	-28	\$60.00 / SF	for	20,172 SF			\$1,210,313
Secondary Window System	Curtain Wall								
% of Windows That are this Type	25%	EUL	C-RUL	Cost / Unit		Quantity	Units	=	Total Value
Installed in	1964	50	-8	\$110.00 / SF	for	6,724 SF			\$739,636



Services - Elevators

Primary Conveyance/Elevators	Elevator, Hydraulic, Machine/Controller/Cab								
Quantity of Stops	3	EUL	C-RUL	Cost / Unit		Quantity	Units	=	Total Value
Installed in	2012	30	20	\$25,000.00 / STOP	for	3 STOP			\$75,000
Secondary Conveyance/Elevators	-								
Quantity of Stops	0	EUL	C-RUL	Cost / Unit		Quantity	Units	=	Total Value
Installed in	-	-	N/A	- / -	for	0 -			\$0

Services - Plumbing

Primary Plumbing System	Supply & Sanitary, Medium Density (Includes Fixtures)								
Area of building served	100%	EUL	C-RUL	Cost / Unit		Quantity	Units	=	Total Value
Installed in	1964	40	-18	\$15.00 / GSF	for	112,066 GSF			\$1,680,990
Secondary Plumbing System	-								
Area of building served	0%	EUL	C-RUL	Cost / Unit		Quantity	Units	=	Total Value
Installed in	-	-	N/A	- / -	for	-	-		\$0



Services - Cooling - Central System

Primary Central Cooling System	None								
Area of building served	0%	EUL	C-RUL	Cost / Unit		Quantity	Units	=	Total Value
Installed in	-	-	N/A	- / -	for	-	-		\$0
Secondary Plumbing System	-								
Area of building served	0%	EUL	C-RUL	Cost / Unit		Quantity	Units	=	Total Value
Installed in	-	-	N/A	- / -	for	-	-		\$0

Services - Heating - Central System

Primary Heating System	Boiler(s)/System - Solid Fuel (Wood/Pellet)								
Area of building served	100%	EUL	C-RUL	Cost / Unit		Quantity	Units	=	Total Value
Installed in	1995	25	-2	\$250.00 / MBH	for	3,202 MBH			\$800,471
Secondary Heating System	-								
Area of building served	0%	EUL	C-RUL	Cost / Unit		Quantity	Units	=	Total Value
Installed in	-	-	N/A	- / -	for	-	-		\$0



2022 School Facilities Inventory Report

Facility Name: **HARTFORD SD | HARTFORD HIGH SCHOOL | 37 HIGHLAND AVENUE, WHITE RIVER JCT 5001 - High (9 thru 12) - Main Building**

Services - HVAC Distribution

Primary HVAC Distribution System **Forced Air System (AHUs, Ductwork, VAVs), 2-Pipe System**

Area of building served	100%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	1986	30	-6	\$18.00 / GSF	112,066	GSF	\$2,017,188



Secondary HVAC Distribution System -

Area of building served	0%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	-	-	N/A	- / -	-	-	\$0

Services - Package Systems

Primary HVAC Package Unit & Splits **None**

Area of building served	0%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	-	-	N/A	- / -	-	-	\$0

Secondary HVAC Package Unit & Splits -

Area of building served	0%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	-	-	N/A	- / -	-	-	\$0

Services - Fire Suppression

Primary Fire Suppression System **Sprinkler System, Medium Density/Complexity**

Area of building served	50%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	1986	40	4	\$5.00 / GSF	56,033	GSF	\$280,165

Secondary Fire Suppression System **Kitchen Hood or Computer Center Suppression System**

Area of building served	1 EA	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	1986	20	-16	\$10,000.00 / EA	1	EA	\$10,000



Services - Fire Alarm System

Primary Fire Suppression System **Modern Addressable Fire Alarm System**

Area of building served	100%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	1986	20	-16	\$3.00 / SF	112,066	SF	\$336,198



Secondary Fire Suppression System -

Area of building served	0%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	-	-	N/A	- / -	-	-	\$0

Services - Security Systems

Primary Security & Low Volt System **Security & Low Voltage Systems - Average**

Area of building served	50%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	2015	15	8	\$4.00 / GSF	56,033	GSF	\$224,132

Secondary Security & Low Volt System -

Area of building served	0%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	-	-	N/A	- / -	-	-	\$0

Services - Electrical Distribution/Infrastructure

Electrical Distribution/Infrastructure **Main Distribution Panel w/Sub Panels and Generator/UPS - Medium Density**

Area of building served	100%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	1964	40	-18	\$22.00 / GSF	112,066	GSF	\$2,465,452



Services - Solar Power (PV)

Solar (Electric Generation) Provided **None**

Owned/Maintained by School -

Quantity of Panels 0

Installed in -

Value of Solar PV Panels: -

EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
-	N/A	- / -	-	-	\$0

Ancillary Structures

Ancillary Structures **None**

Total SF of Ancillary Structures -

Installed in -

EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
-	N/A	- / -	-	-	\$0

Secondary Ancillary Structures -

Total SF of Secondary Ancillary Structures 0

Installed in -

EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
-	N/A	- / -	-	-	\$0

Additional Comments

Elevator shared with HACTC

2022 School Facilities Inventory Report

Facility Name: **HARTFORD SD | HARTFORD HIGH SCHOOL | 37 HIGHLAND AVENUE, WHITE RIVER JCT 5001 - High (9 thru 12) - Main Building**

Explanation of Terms

Projected Capital Planning Cash Flow	The estimated replacement costs of systems as they expire annually.
Facility Condition Index (FCI)	The cost -weighted depleted value of the building compared to the total value of all its systems; overall percent of building useful life consumed by years in service.
Total Value of Assets	The total estimated replacement cost of all the assets listed in the form.
Value of Assets per GSF	The Total Value of all Assets in the form divide by the Gross Square Footage (GSF) of the building.
Facility Condition Index (FCI) Compared to Portfolio	The Facility Condition Index (FCI) of the building overlayed on the chart of FCI's for all buildings in the portfolio. Indicated by a red line in the chart.
Calculated Remaining Useful Life(C-RUL)	The current number of remaining years a system may be expected to perform in designed service.
Expected Useful Life (EUL)	The total number of years a system can be expected to perform in designed service when new.
Gross Square Footage (GSF)	The total square footage contained within the building for all floors/levels.
Cost per Unit	The estimated base cost for a single unit of a system. When multiplied by Quantity results in the total system cost.
Quantity	The amount of a system present in a building. When multiplied by the Cost per Unit results in the total system cost.
Units	The expressed unit of measure for a given system (GSF, EACH, TON, etc).
Ancillary Structures	Buildings on site that are typically known as portables, relocatables or temporary buildings.
