

MONOKO, LLC

1037 Peninsula Avenue
Tarpon Springs, FL 34689-2125
E-mail Address: MonokoLLC@aol.com

(727) 940-3244
(727) 279-8795 Fax

Submission No.: 23f, Traffic Control Plans D62N & S

Date: June 24, 2015

Vermont Department of Transportation
Northeast Regional Construction Office

Attn: Mr. Ron Gray
347 Emerson Falls Road, Suite 5
St. Johnsbury, VT 05819
(Phone) (802) 751-3295; (Cell) (802) 793-3161
(Fax) (802) 751-3297; Ron.Gray@state.vt.us

Description: Proposal/Contract Number: Bradford-Newbury IM BPNT (14)
Letting Date: 10/10/14; Award Date: 11/03/14
Project Description: Bridge Painting of Five Bridges
In the Towns of Bradford & Newbury, VT
Contract Amount: \$4,327,785.00; Completion Date: 08/26/16

Contractor: MONOKO, LLC


Reviewed & Approved By: *Keri Monokandilos*

Keri Monokandilos, Manager

Date: 06/24/2015

Engineer: Peter Hodgson, Resident Engineer
347 Emerson Falls Road, Suite 5
St. Johnsbury, VT 05819
802-748-2447; 802-793-1878 cell
pete.hodgson@state.vt.us
Mark. Sargent@state.vt.us
pnmcdonald@gpinet.com
ron.gray@state.vt.us

Revision:

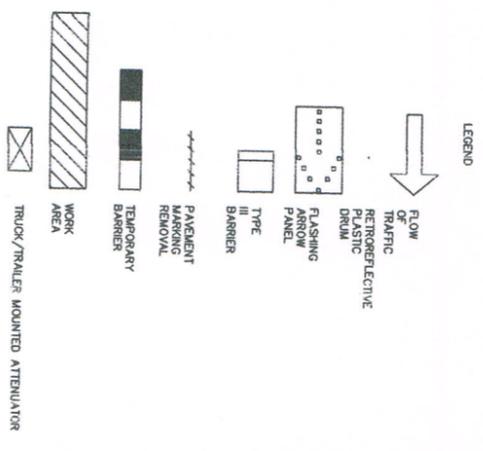

- TRAFFIC CONTROL NOTES - 191E**
1. THE EXISTING SPEED LIMIT FOR I-91 IS 65 MPH. THE SPEED LIMIT WILL BE REDUCED TO 50 MPH IN THE WORK ZONE FOR THIS PHASE OF THE PROJECT. THE SPEED LIMIT WILL BE RESTORED TO 65 MPH UPON COMPLETION OF THE PROJECT. THE SPEED REDUCTION AREA SHALL BE COMPLETELY CONEDED.
 2. CONSTRUCTION SIGNS SHALL BE INSTALLED AS NOT TO OBSTRUCT EXISTING SIGNS.
 3. SOLID SUBSTRATE CONSTRUCTION SIGNS SHALL HAVE RETROREFLECTIVE PLASTIC ON EXCEEDING THE "AMERICAN ASSOCIATION OF STATE HIGHWAY AND TRANSPORTATION OFFICIALS" (ASTM) M 288 "AMERICAN SOCIETY FOR TESTING AND MATERIALS" (ASTM) D 49560 TYPE VI UNLESS OTHERWISE NOTED.
 4. SOLID SUBSTRATE CONSTRUCTION SIGNS SHALL HAVE RETROREFLECTIVE SHEETING EQUAL TO OR EXCEEDING THE "AMERICAN ASSOCIATION OF STATE HIGHWAY AND TRANSPORTATION OFFICIALS" (ASTM) M 288 "AMERICAN SOCIETY FOR TESTING AND MATERIALS" (ASTM) D 49560 TYPE VI UNLESS OTHERWISE NOTED.
 5. CONSTRUCTION SIGNS SHALL BE ERECTED BEFORE THE START OF ANY WORK AND SHALL BE COVERED UNTIL WORK COMMENCES. SIGNS SHALL BE REMOVED UPON COMPLETION OF THE WORK. EACH SIGN SHALL BE ERECTED IN A NEAT AND WORKMANLIKE MANNER.
 6. CONSTRUCTION SIGN COVERS SHALL CONSIST OF A PANEL, PAINTED FLAT BLACK, THE SAME SIZE AS THE SIGN IT COVERS. THE PANEL SHALL BE MADE OF 1/2" THICK ALUMINUM OR ANOTHER MATERIAL THAT WILL DETERMINE BY EXPOSURE TO THE WEATHER DURING THE PROJECT. MOUNTING OF THE PANEL SHALL BE DONE IN SUCH A WAY AS TO NOT DAMAGE THE SIGN FACE MATERIAL.
 7. SIGNS SHALL BE MAINTAINED IN A CLEAN AND LEGIBLE CONDITION. SIGNS SHALL BE REPAIRED OR REPLACED AS NECESSARY. DAMAGED OR DIRTY SIGNS SHALL BE REPAIRED, CLEANED OR REPLACED AS ORDERED BY THE ENGINEER.
 8. NO CROSS-BRACING OR BACK-BRACING TO KEEP POSTS PLUMB WILL BE ALLOWED. CONCRETE FOUNDATIONS, COLLARS OR SOIL BERMING SHALL BE NOT PERMITTED. CONSTRUCTION SIGNS SHALL BE PLACED ON TWO POSTS.


WORK ACTIVITIES

WORK UNDER THIS PHASE WILL BE THE CLEANING AND PAINTING OF ALL STEEL COMPONENTS OF BOTH BRIDGE NOS. D62S AND D62N. THE LEFT TRAVELPATH AND SHOULDER ON I-91 SOUTHBOUND WILL BE CLOSED TO TRAFFIC DURING THIS CONSTRUCTION PHASE.

ALL EQUIPMENT INCLUDING BUT NOT LIMITED TO DUST COLLECTION SYSTEMS, AIRCICLE UNIT, COMPRESSORS, HAZARDOUS WASTE STORAGE CONTAINERS AND HAND WASH FACILITIES WILL BE LOCATED BEHIND PRECAST CONCRETE PROTECTIVE BARRIER ON THE I-91 SB PAVEMENT SURFACE NORTH OF BRIDGE D62S.

ALL WORK WILL BE PERFORMED BEHIND PRECAST CONCRETE BARRIER. WORKERS, EQUIPMENT AND SUPPLIES WILL BE DELIVERED THROUGH THE OPENING IN THE PRECAST CONCRETE PROTECTIVE BARRIER ON THE LEFT SHOULDER SOUTH OF BRIDGE D62S. ALL EQUIPMENT AND SUPPLIES WILL BE STORED BEHIND PROTECTIVE BARRIER.

NO WORK WILL BE PERFORMED FROM FAIRGROUND ROAD OVER I-91.

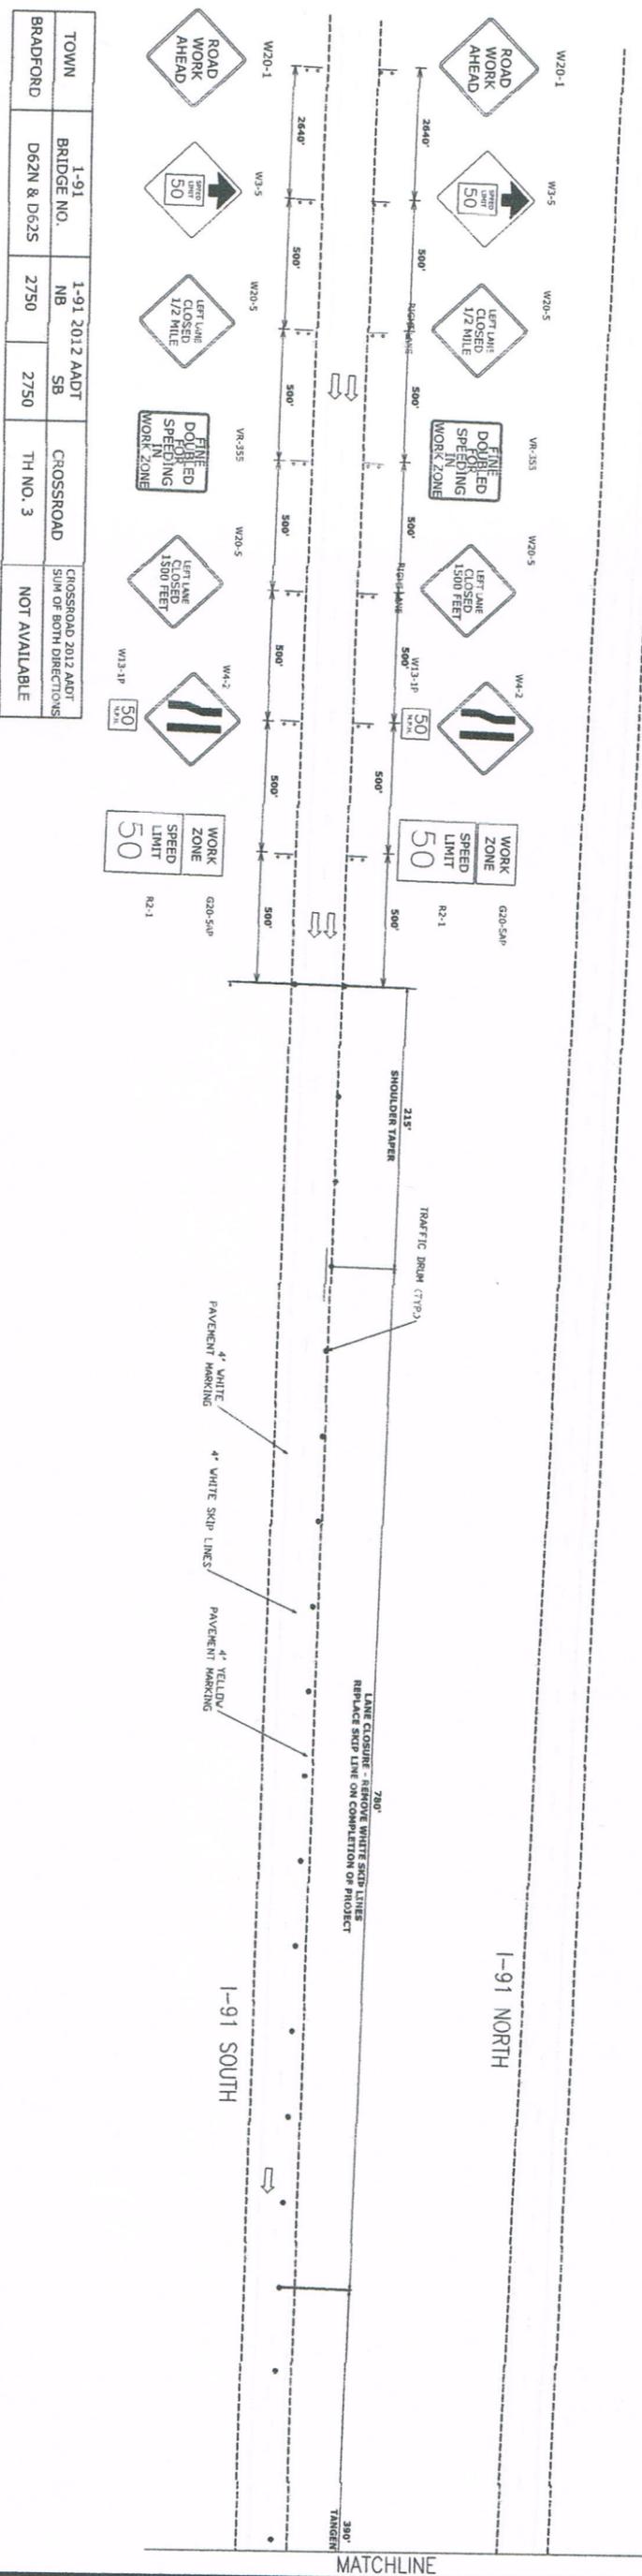

TOWN	BRADFORD	BRIDGE NO.	D62N & D62S	1-91 2012 AADT	NB	2750	SB	2750	CROSSROAD	TH NO. 3	CROSSROAD 2012 AADT	SLIP OF BOTH DIRECTIONS	NOT AVAILABLE
------	----------	------------	-------------	----------------	----	------	----	------	-----------	----------	---------------------	-------------------------	---------------



Alfred Benesch & Company • www.benesch.com
 90 National Drive • Glastonbury, Connecticut 06033
 Phone: (860) 633-8341 • Fax: (860) 633-1088

Prepared For:
MONOKO, LLC.

1037 PENINSULA AVENUE
 TARPON SPRINGS, FL
 (737) 940 - 3244

TRAFFIC CONTROL PLAN
LEFT LANE AND SHOULDER CLOSURE
BRIDGE D62
I-91 SB



PROJECT NO.: 70270

DRAWN BY: CMS



DATE: MAY 2015

CHECKED BY: JAK





DRAWING NO.:
 I-91 SB LEFT
 1 OF 2

DATE	REVISION

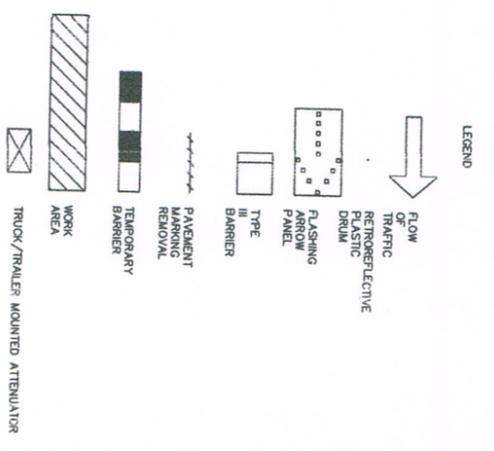

NOTE: LEADING END OF TEMPORARY PRECAST BARRIER TO BE PROTECTED BY TEMPORARY SAND INERTIAL ATTENUATION SYSTEM OR TRUCK/TRAILER MOUNTED ATTENUATOR SYSTEM ADEQUATE FOR A SPEED OF 50 MPH

⊗ - INDICATES MODULE LOCATION AND MASS OF SAND IN POUNDS FOR EACH MODULE

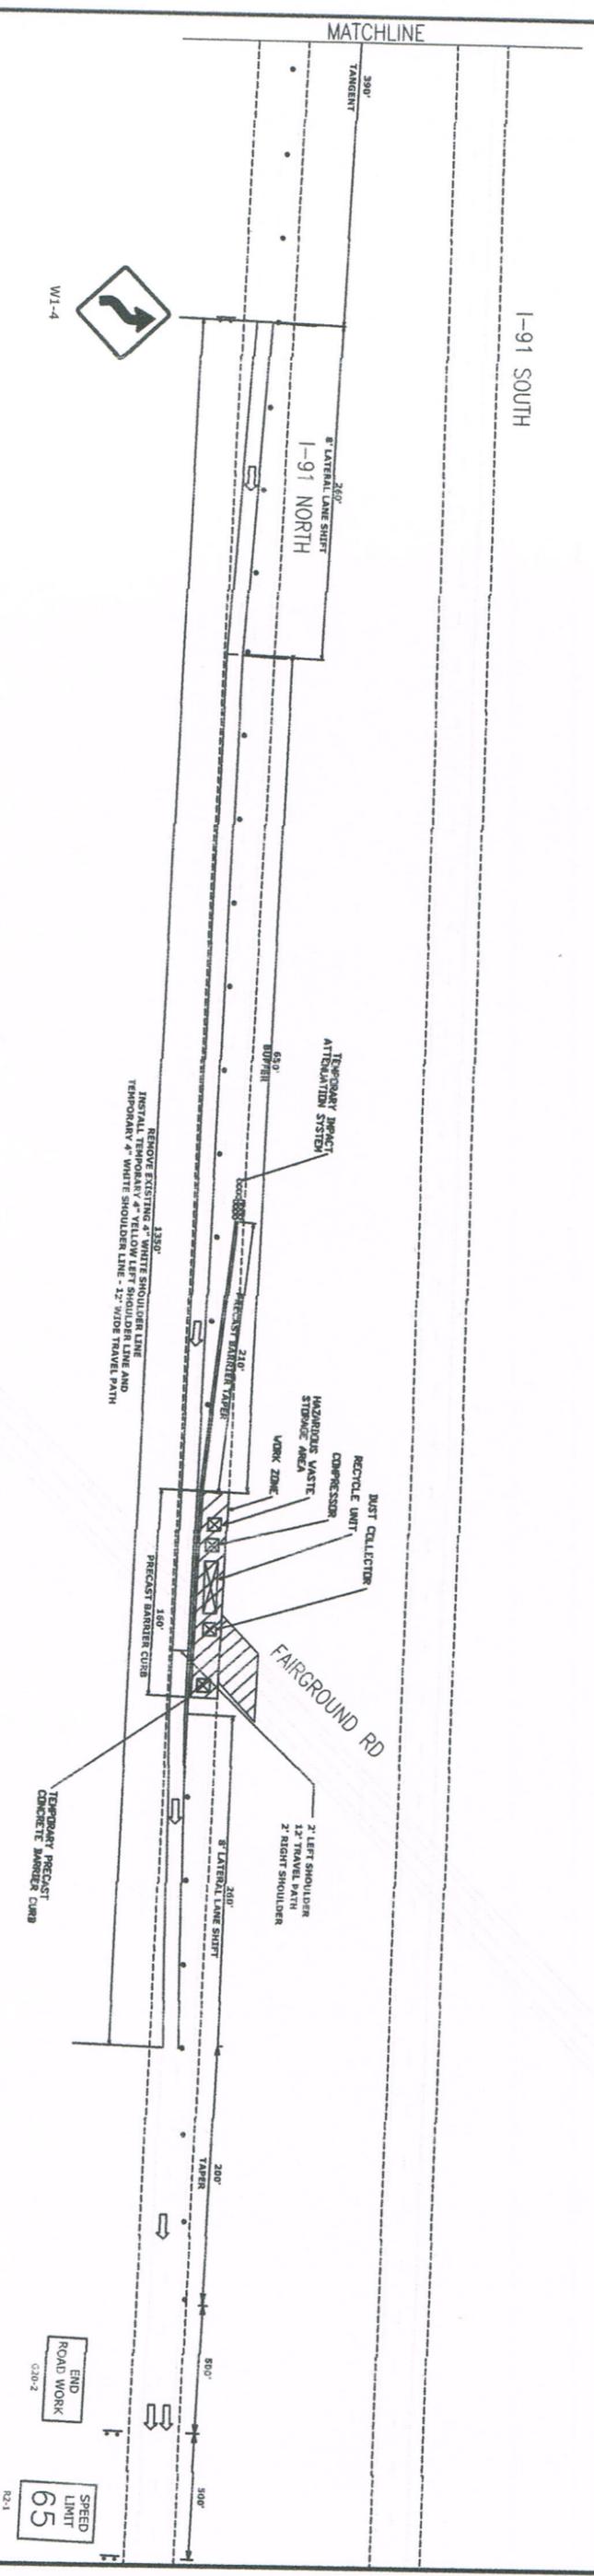

Alfred Benesch & Company • www.benesch.com
90 National Drive • Glastonbury, Connecticut 06033
Phone: (860) 633-8341 • Fax: (860) 633-1098

Prepared For:
MONOKO, LLC.

**1037 PENINSULA AVENUE
TARPOON SPRINGS, FL
(737) 940 - 3244**

**TRAFFIC CONTROL PLAN
LEFT LANE AND SHOULDER CLOSURE
BRIDGE D62
I-91 NB**



PROJECT NO.: 70270

DRAWN BY: CMS

DATE: MAY 2015

CHECKED BY: JAK



DRAWING NO.:
I-91 NB LEFT
2 OF 2

DATE	REVISION
