

### 2022 School Facilities Inventory Report

Facility Name: **LAMOILLE SOUTH UNIFIED UNION SD | ELMORE SCHOOL | 1199 VT ROUTE 12, LAKE ELMORE 5657 - Elementary (1 thru 4) - Main Building**


March 29, 2022

Total Value of Assets (Does Not Include Site/Structure/Walls/Interiors) **\$176,829**



GPS: 44.54087195395189, -72.52303581806594

#### Relative Asset Values


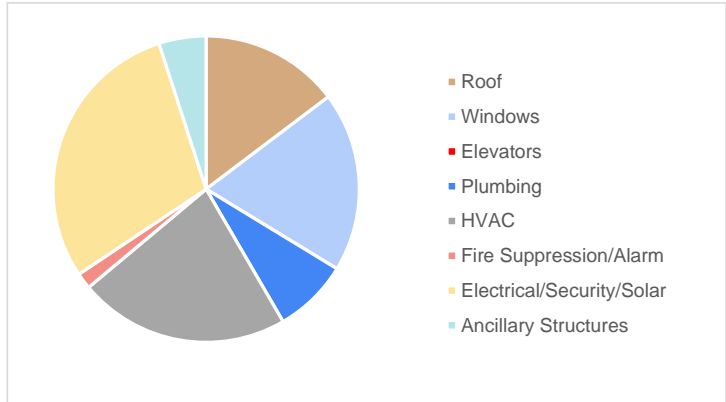


Value of Assets/GSF **\$88.41**




Site Plan - Google Earth

#### Projected Capital Planning Cash Flow

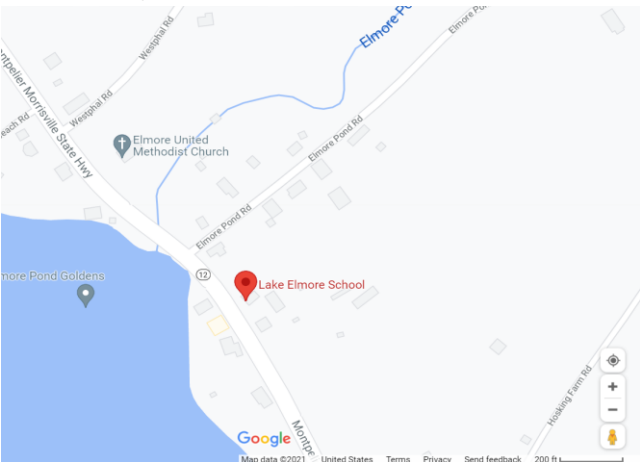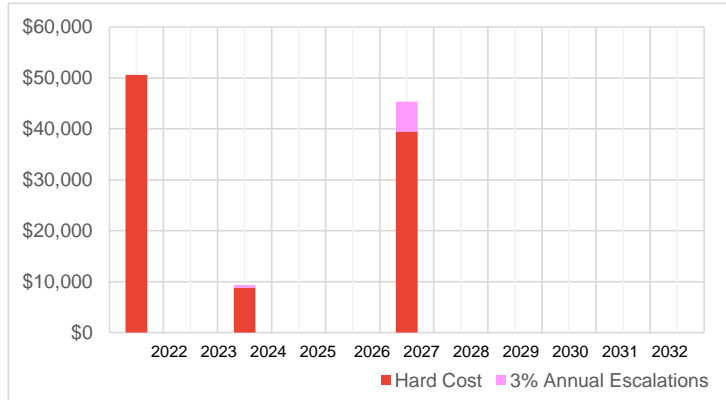

Location Plan - Google Maps

#### Facility Condition Index (FCI) Compared to Portfolio

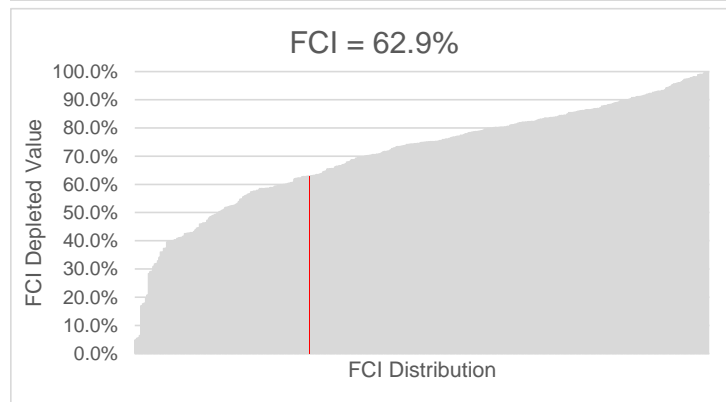

(See Last Page for Explanation of Terms)

### 2022 School Facilities Inventory Report

Facility Name: **LAMOILLE SOUTH UNIFIED UNION SD | ELMORE SCHOOL | 1199 VT ROUTE 12, LAKE ELMORE 5657 - Elementary (1 thru 4) - Main Building**


#### Respondent Information

Date/Time Completed **2021-12-13 - 12:27 PM**  
 Respondent Name **Brian Rafferty**  
 Respondent Title **Director of Facilities**  
 Respondent Email **brian.rafferty@lsuu.org**  
 Respondent Phone Number **(802) 888-4600**

#### Facility Information

School Type **Elementary (1 thru 4)**  
 Building Identification **Main Building**  
 Stories **1**  
 Building Area **2000 (Gross Square Footage - GSF)**  
 Year Constructed **1850**  
 Year of Last Major Renovation **2010**  
 FCI (Depleted Value) **62.9%**

#### Environmental & Safety Issues

Hazardous Materials **Maybe**   
 Hazardous (HZD) Materials include **Lead paint**  
 HZD Issues are **Minor**  
 HZD Issues include **An old building that has to assume lead paint, has vinyl siding covering the exterior. 1970's windows probably have pcb's, any exposed paint is stable**

Indoor Air Quality (IAQ) Issues **No**  
 IAQ Issues include -  
 IAQ Issues are -  
 IAQ Issues include -


Fire or Life/Safety (FL/S) Issues **No**  
 FL/S Issues are -

Other Risk Factors **No**  
 Other Risk Factors include -  
 Other Risk Factors are -

#### Handicap Accessibility (ADA) Issues

Handicap Accessibility (ADA) Issues **No**  
 ADA Issues are **N/A**  
 ADA Issues include **N/A**

#### Utilities - Adequacy

IT / Internet Service **Adequate**  
 Building Wi-Fi Coverage **Adequate**  
 Cellular Reception **Inadequate**   
 Water Service Pressure **Adequate**  
 Natural Gas/Propane Pressure **N/A**  
 Electrical Capacity **Adequate**

### 2022 School Facilities Inventory Report

Facility Name: **LAMOILLE SOUTH UNIFIED UNION SD | ELMORE SCHOOL | 1199 VT ROUTE 12, LAKE ELMORE 5657 - Elementary (1 thru 4) - Main Building**

#### Building Envelope - Roof

Roof 1 is <b>Metal</b>	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Covers <b>100%</b>	40	28	\$13.00 / SF	2,000	SF	\$26,000
Installed in <b>2010</b>						
Roof 2 is -	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Covers <b>0%</b>	-	N/A	- / -	-	-	\$0
Installed in -						
Roof 3 is -	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Covers <b>0%</b>	-	N/A	- / -	-	-	\$0
Installed in -						
Roof 4 is -	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Covers <b>0%</b>	-	N/A	- / -	-	-	\$0
Installed in -						

#### Building Envelope - Windows

Primary Window System <b>Window, Wood-Frame</b>	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
% of Windows That are this Type <b>100%</b>	30	-22	\$70.00 / SF	480	SF	\$33,600
Installed in <b>1970</b>						
Secondary Window System -	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
% of Windows That are this Type <b>0%</b>	-	N/A	- / -	-	-	\$0
Installed in -						

#### Services - Elevators

Primary Conveyance/Elevators <b>None</b>	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Quantity of Stops <b>0</b>	-	N/A	- / -	0	-	\$0
Installed in -						
Secondary Conveyance/Elevators -	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Quantity of Stops <b>0</b>	-	N/A	- / -	0	-	\$0
Installed in -						

#### Services - Plumbing

Primary Plumbing System <b>Supply &amp; Sanitary, Low Density (Includes Fixtures)</b>	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Area of building served <b>100%</b>	40	-32	\$7.00 / GSF	2,000	GSF	\$14,000
Installed in <b>1950</b>						
Secondary Plumbing System -	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Area of building served <b>0%</b>	-	N/A	- / -	-	-	\$0
Installed in -						

#### Services - Cooling - Central System

Primary Central Cooling System <b>None</b>	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Area of building served <b>0%</b>	-	N/A	- / -	-	-	\$0
Installed in -						
Secondary Plumbing System -	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Area of building served <b>0%</b>	-	N/A	- / -	-	-	\$0
Installed in -						

#### Services - Heating - Central System

Primary Heating System <b>Boiler(s)/System - Fuel Oil</b>	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Area of building served <b>100%</b>	30	6	\$60.00 / MBH	57	MBH	\$3,429
Installed in <b>1998</b>						
Secondary Heating System -	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Area of building served <b>0%</b>	-	N/A	- / -	-	-	\$0
Installed in -						

### 2022 School Facilities Inventory Report

Facility Name: **LAMOILLE SOUTH UNIFIED UNION SD | ELMORE SCHOOL | 1199 VT ROUTE 12, LAKE ELMORE 5657 - Elementary (1 thru 4) - Main Building**

#### Services - HVAC Distribution

Primary HVAC Distribution System **Forced Air System (AHUs, Ductwork, VAVs), 2-Pipe System**

Area of building served	100%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	1998	30	6	\$18.00 / GSF	2,000	GSF	\$36,000

Secondary HVAC Distribution System -

Area of building served	0%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	-	-	N/A	- / -	-	-	\$0

#### Services - Package Systems

Primary HVAC Package Unit & Splits **None**

Area of building served	0%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	-	-	N/A	- / -	-	-	\$0

Secondary HVAC Package Unit & Splits -

Area of building served	0%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	-	-	N/A	- / -	-	-	\$0

#### Services - Fire Suppression

Primary Fire Suppression System **None**

Area of building served	0%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	-	-	N/A	- / -	-	-	\$0

Secondary Fire Suppression System -

Area of building served	0%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	-	-	N/A	- / -	-	-	\$0

#### Services - Fire Alarm System

Primary Fire Suppression System **Older type Zoned System**

Area of building served	100%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	1998	20	-4	\$1.50 / GSF	2,000	GSF	\$3,000

Secondary Fire Suppression System -

Area of building served	0%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	-	-	N/A	- / -	-	-	\$0

#### Services - Security Systems

Primary Security & Low Volt System **Security & Low Voltage Systems - Average**

Area of building served	100%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	2020	15	13	\$4.00 / GSF	2,000	GSF	\$8,000

Secondary Security & Low Volt System -

Area of building served	0%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	-	-	N/A	- / -	-	-	\$0

#### Services - Electrical Distribution/Infrastructure

Electrical Distribution/Infrastructure **Main Distribution Panel w/Sub Panels and Generator/UPS - Medium Density**

Area of building served	100%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	2010	40	28	\$22.00 / GSF	2,000	GSF	\$44,000

#### Services - Solar Power (PV)

Solar (Electric Generation) Provided **None**

Owned/Maintained by School -

Quantity of Panels 0

Area of building served	0%	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	-	-	N/A	- / -	-	-	\$0

Value of Solar PV Panels: -

#### Ancillary Structures

Ancillary Structures **Relocatable Building - Classroom/Office - Basic/Portable**

Total SF of Ancillary Structures	80	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	2010	15	3	\$110.00 / SF	80	SF	\$8,800

Secondary Ancillary Structures -

Total SF of Secondary Ancillary Structures	0	EUL	C-RUL	Cost / Unit	Quantity	Units	Total Value
Installed in	-	-	N/A	- / -	-	-	\$0

#### Additional Comments

**2022 School Facilities Inventory Report**

Facility Name: **LAMOILLE SOUTH UNIFIED UNION SD | ELMORE SCHOOL | 1199 VT ROUTE 12, LAKE ELMORE 5657 - Elementary (1 thru 4) - Main Building**

## Explanation of Terms

<b>Projected Capital Planning Cash Flow</b>	The estimated replacement costs of systems as they expire annually.
<b>Facility Condition Index (FCI)</b>	The cost -weighted depleted value of the building compared to the total value of all its systems; overall percent of building useful life consumed by years in service.
<b>Total Value of Assets</b>	The total estimated replacement cost of all the assets listed in the form.
<b>Value of Assets per GSF</b>	The Total Value of all Assets in the form divide by the Gross Square Footage (GSF) of the building.
<b>Facility Condition Index (FCI) Compared to Portfolio</b>	The Facility Condition Index (FCI) of the building overlaid on the chart of FCI's for all buildings in the portfolio. Indicated by a red line in the chart.
<b>Calculated Remaining Useful Life( C-RUL)</b>	The current number of remaining years a system may be expected to perform in designed service.
<b>Expected Useful Life (EUL)</b>	The total number of years a system can be expected to perform in designed service when new.
<b>Gross Square Footage (GSF)</b>	The total square footage contained within the building for all floors/levels.
<b>Cost per Unit</b>	The estimated base cost for a single unit of a system. When multiplied by Quantity results in the total system cost.
<b>Quantity</b>	The amount of a system present in a building. When multiplied by the Cost per Unit results in the total system cost.
<b>Units</b>	The expressed unit of measure for a given system (GSF, EACH, TON, etc).
<b>Ancillary Structures</b>	Buildings on site that are typically known as portables, relocatables or temporary buildings.
