VERMONT

State of Vermont
PDD/Structures Design Section
National Life Building – Drawer 33
Montpelier, VT 05633-5001
www.aot.state.vt.us

Agency of Transportation

[phone] 802-828-01611
[fax] 802-828-3566
[ttd] 800-253-0191

February 5, 2015

J. P. Sicard, Inc.
PO Box 508
Barton, VT 05822

Project Name: Randolph BRO 1444(57)

Structure Identification: TH65 (Palmer Road) Bridge 35

The steel bearing shim fabrication drawing associated with Item 531.17, Bearing Device Assembly, Steel Reinforced Elastomeric Pad, has been reviewed and is being returned herewith.

Please incorporate all review comments in red and resubmit.

Sincerely,

Todd A. Sumner P.E.
Project Manager

VTrans Working to Get You There
Vermont Agency of Transportation

BILL OF MATERIAL

QTY.	MARK	SHAPE	LENGTH		REMARKS
8		1'-Ø½ x ¼" Stl PL	1	Ø½	Domestic Steel PL

Please specify steel grade. Per specs it should be grade 36 or 50.

Please provide required material certifications.

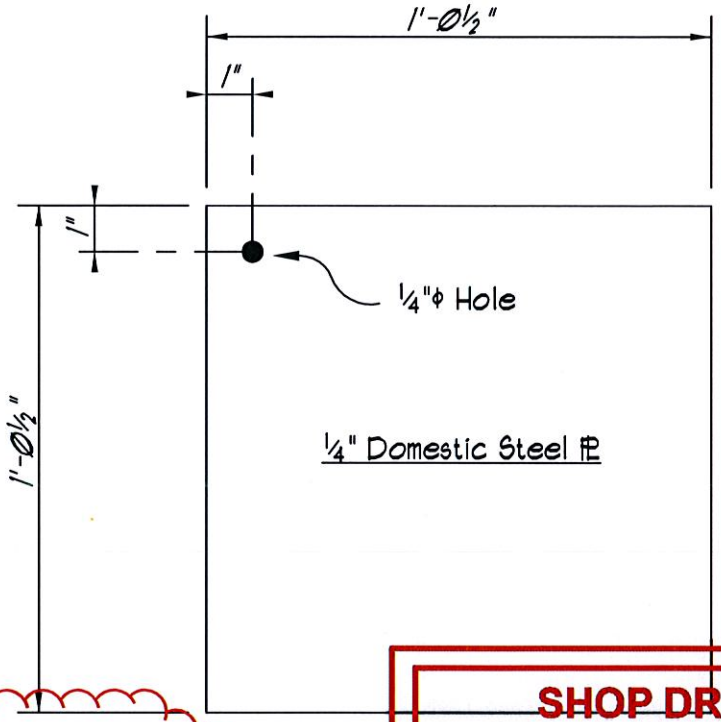

Vermont Agency of Transportation
RECEIVED
ON: February 3, 2015
and Checked for
CONFORMANCE
BY: T. A. Sumner DATE: 02/05/15

Please add the following notes:

1. Prior to galvanizing, all corners and edges of steel plates, shapes, etc., shall be ground to a 1/16" (1.6mm) radius.

2. Surfaces to be galvanized shall be zinc coated in conformance with AASHTO M 111M/ M111 or, when applicable, AASHTO M 232M/ M232.

Please specify steel grade. Per specs it should be grade 36 or 50.

General Notes:

Domestic Steel PL Cut As Shown.
Standard Hot-Dip Galv'd Per Specs.

SHOP DRAWING REVIEW

Make 8 Shims

REVIEWED AS REQUIRED BY THE CONSTRUCTION CONTRACT DOCUMENTS AND APPROVED, BUT ONLY FOR CONFORMANCE TO THE DESIGN CONCEPT OF THE WORK, AND SUBJECT TO FURTHER LIMITATIONS AND REQUIREMENTS CONTAINED IN THE CONSTRUCTION CONTRACT DOCUMENTS.

☐ REJECTED ☒ REVISE AND RESUBMIT ☐ APPROVED AS NOTED

CORRECTIONS OR COMMENTS MADE ON THE SHOP DRAWINGS DURING THIS REVIEW DID NOT RELIEVE CONTRACTOR FROM COMPLIANCEWITH REQUIREMENTS OF THE DRAWINGS AND SPECIFICATIONS. THIS CHECK IS ONLY FOR REVIEW OF GENERAL CONFORMANCE WITH THE DESIGN CONCEPT OF THE PROJECT AND GENERAL COMPLIANCE WITH THE INFORMATION GIVEN IN THE CONTRACT DOCUMENTS. THE CONTRACTOR IS RESPOINSIBLE FOR: CONFIRMING AND CORRELATING ALL QUANTITIES AND DIMENSIONS: SELECTING FABRICATION PROCESSES AND TECHNIQUES OF CONSTRUCTION: COORDINATING THEIR WORK WITH THAT OF ALL OTHER TRADES: AND PERFORMING THEIR WORK IN A SAFE AND SATISFACTORY MANNER.

CLD Consulting Engineers
540 Commercial Street
Manchester, NH 03101
603-668-8223

Job Number: 12-0175
Reviewed by: NDC
Date: 2/4/2015

DESCRIPTION: Steel Shim PLs Per Customer Information

OSGOOD WELDING 144 Grissom Lane, Claremont, N.H. 03743 Phone: 603-643-1703	PROJECT: Randolph BRO 1444 (51)	DR. CBB • WFM	HOLES ¼"ϕ	DATE 2-03-2015	JOB NO.
	LOCATION: Town Highway 65 (Palmer Rd) Bridge 35	CH.	BOLTS	APPROVED	SK. NO. SK-1
	GEN'L. CONTR.: Town of Randolph, County of Orange, Vt	PAINT None - Galv'd Per Specs			
