Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	%	Resource	Budgeted Cost
1000	Mobilize	10d	10d *	30SEP13 A	11OCT13	39d	0		0
1010	Set Up Office Trailer	10d	10d *	30SEP13 A	11OCT13	39d	0		0
1020	Install Sign Package	5d	5d *	14OCT13 A	18OCT13	34d	0		0
1030	Install Erosion Control	5d	5d *	21OCT13 A	25OCT13	29d	0		0
1040	Install Stone Fill Crane Pads	6d	6d *	23OCT13 A	30OCT13	26d	0		0
1050	Install Coffer Dam	10d	10d *	31OCT13 A	13NOV13	16d	0		0
1060	Close Rt 17 Install New Box Culvert	1h	1h *	16NOV13 A	18NOV13	14d	0		0
1070	Remove Coffer Dam	5d	5d *	18NOV13 A	22NOV13	9d	0		0
1080	Install Stone Fill	5d	5d *	20NOV13 A	26NOV13	7d	0		0
1090	Remove Crane Pads	5d	5d *	20NOV13 A	26NOV13	7d	0		0
1100	Install Topsoil Seed & Mulch	3d	3d *	25NOV13 A	27NOV13	6d	0		0
1110	Remove Erosion Control	2d	2d *	28NOV13 A	29NOV13	4d	0		0
1120	Pave	2d	2d *	02DEC13 A	03DEC13	2d	0		0
1130	Install Guard Rail	1d	1d *	04DEC13 A	04DEC13	1d	0		0
1140	Line Stripe	1d	1d *	05DEC13 A	05DEC13	0	0		0
1150	Demobilize	1d	1d *	06DEC13 A	06DEC13	-1d	0		0

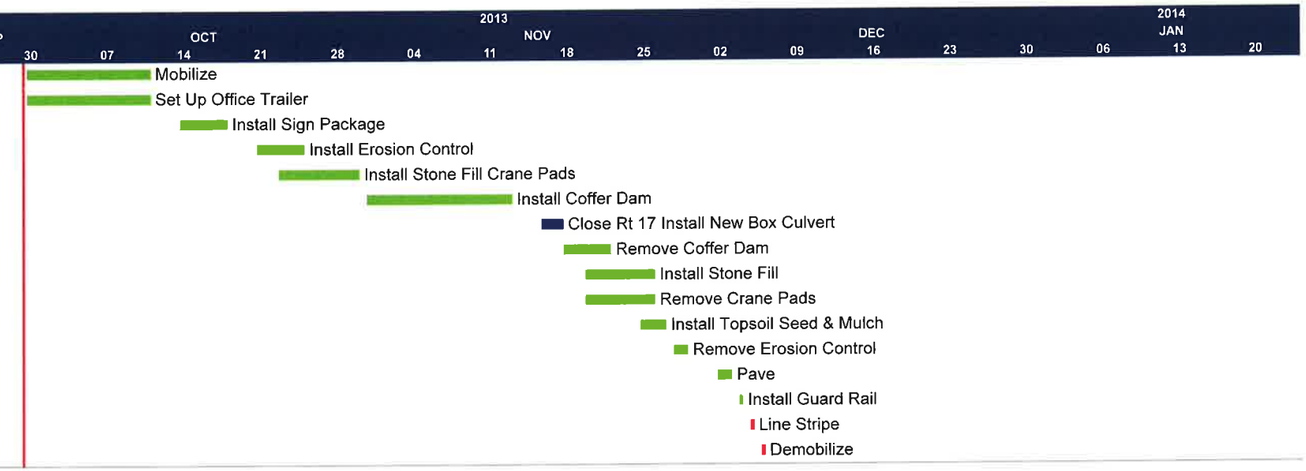

Start date 30SEP13
Finish date 06DEC13
Data date 30SEP13
Run date 09SEP13
Page number 1A

© Primavera Systems, Inc.

SD Ireland Concrete Construction
Addison STP CULV (14)

Early bar
Progress bar
Critical bar
Summary bar
Start milestone point
Finish milestone point
