ID	Task Name	Duration	Start	Finish
1	**Bridge 16 BCP**	**60 hrs**	**Fri 7/18/14**	**Mon 7/21/1**
2	Shutdown Bridge	0 days	Fri 7/18/14	Fri 7/18/14
3	Structure Excavation	4 hrs	Fri 7/18/14	Fri 7/18/14
4	Remove Superstructure	5 hrs	Fri 7/18/14	Sat 7/19/14
5	Remove Abutments	5 hrs	Sat 7/19/14	Sat 7/19/14
6	Setup Crane	4 hrs	Sat 7/19/14	Sat 7/19/14
7	Cut Piles To Grade	2 hrs	Sat 7/19/14	Sat 7/19/14
8	Weld Pile Plates	2 hrs	Sat 7/19/14	Sat 7/19/14
9	Install Abut/WW 1	3 hrs	Sat 7/19/14	Sat 7/19/14
10	Post Tensioning Abut 1	1 hr	Sat 7/19/14	Sat 7/19/14
11	Install Abut/WW 2	3 hrs	Sat 7/19/14	Sat 7/19/14
12	Post Tensioning Abut 2	1 hr	Sat 7/19/14	Sat 7/19/14
13	Water Repellent	4 hrs	Sat 7/19/14	Sat 7/19/14
14	Install Bearings	2 hrs	Sat 7/19/14	Sat 7/19/14
15	Granular Backfill	3 hrs	Sat 7/19/14	Sat 7/19/14
16	Type 4 Stone Fill	4 hrs	Sat 7/19/14	Sat 7/19/14
17	Erect Next Beams	8 hrs	Sat 7/19/14	Sun 7/20/14
18	Install Approach Slab 1	2 hrs	Sun 7/20/14	Sun 7/20/14
19	Install Approach Slab 2	2 hrs	Sun 7/20/14	Sun 7/20/14
20	Rapid Set Concrete	4 hrs	Sun 7/20/14	Sun 7/20/14
21	Rapid Set Concrete Cure Time	12 hrs	Sun 7/20/14	Mon 7/21/14
22	Sand Borrow & Subbase	6 hrs	Sun 7/20/14	Sun 7/20/14
23	Set Up One Lane Traffic	2 hrs	Mon 7/21/14	Mon 7/21/14
24	Re Open Bridge	0 days	Mon 7/21/14	Mon 7/21/14

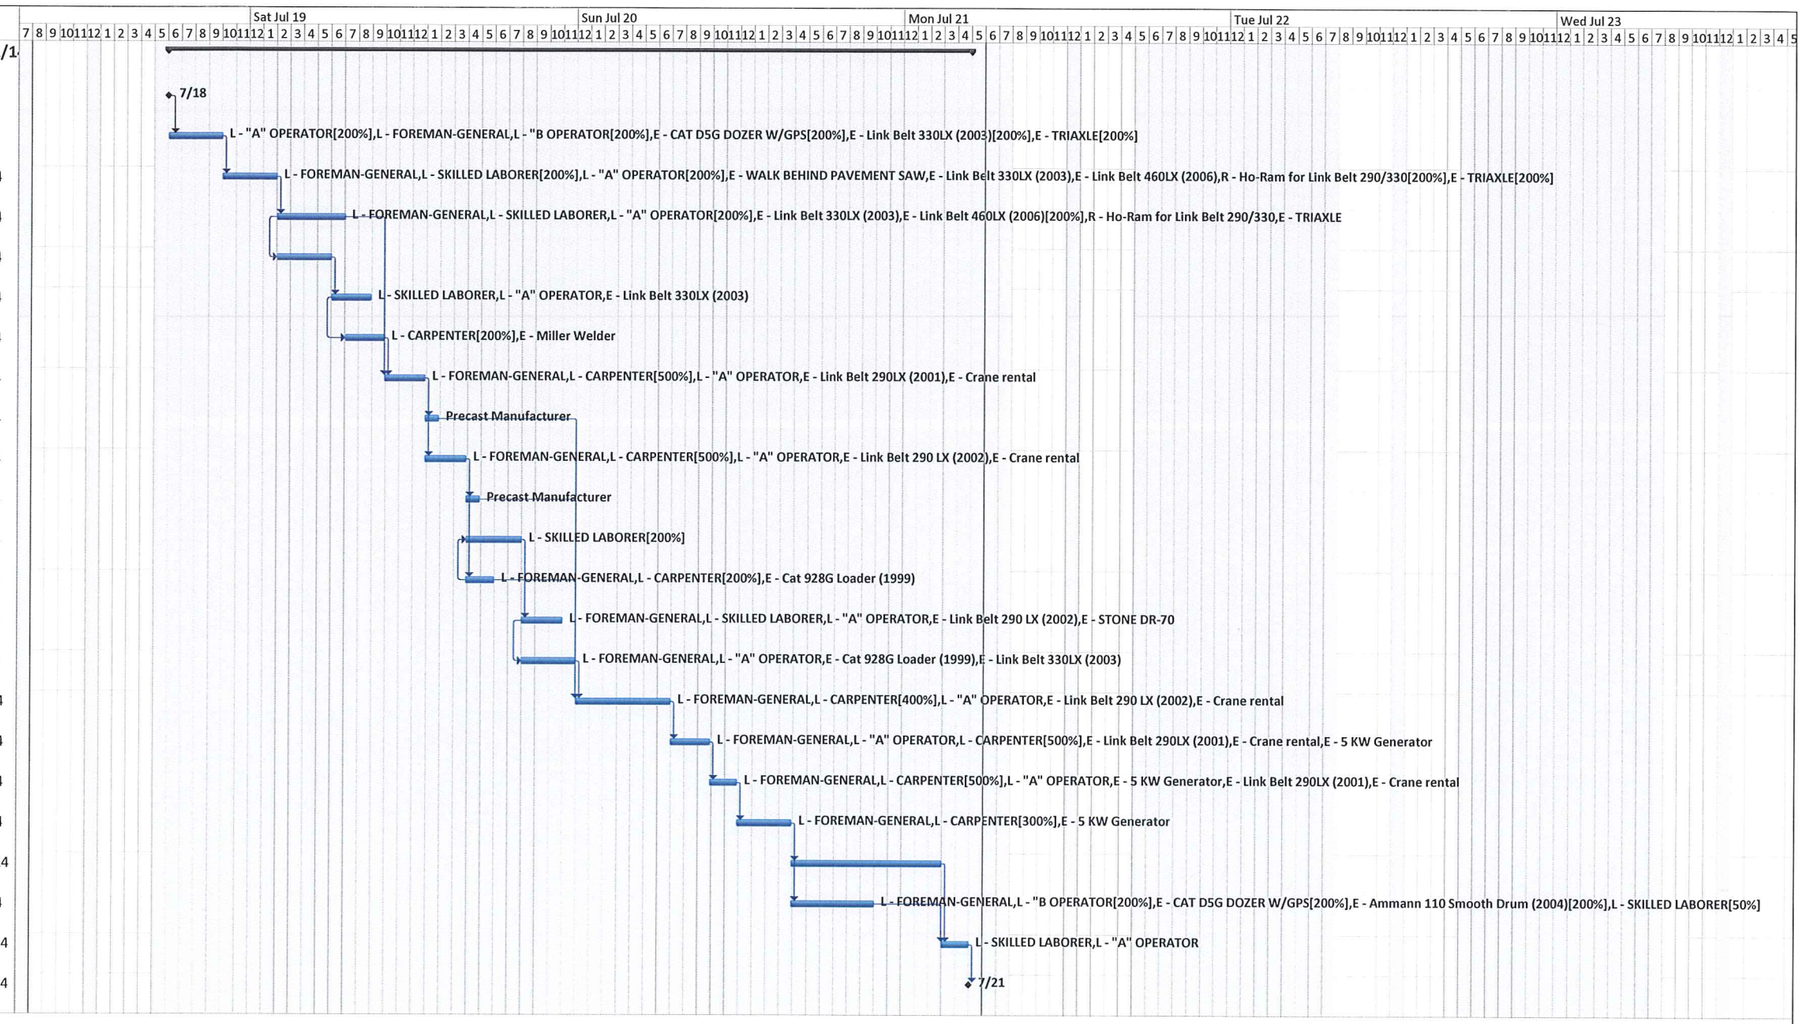

Project: Bridge 16 BCP Hourly
Date: Wed 2/5/14

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | Deadline | Progress
