VTRANS
Bridge 15
Rochester, VT BRF 0162(16)

ID	Task Mode	Task Name	Duration	Start	Finish
1		**Bridge 15 BCP**	**84 hrs**	**Thu 7/10/14**	**Mon 7/14/14**
2		Shutdown Bridge	0 days	Thu 7/10/14	Thu 7/10/14
3		Finish Install Select Piles	14 hrs	Thu 7/10/14	Fri 7/11/14
5		Remove Superstructure	3 hrs	Fri 7/11/14	Fri 7/11/14
4		Structure Excavation	2 hrs	Fri 7/11/14	Fri 7/11/14
6		Remove Abutments	4 hrs	Fri 7/11/14	Fri 7/11/14
7		Setup Crane	4 hrs	Fri 7/11/14	Fri 7/11/14
8		Cut Piles To Grade	2 hrs	Fri 7/11/14	Fri 7/11/14
9		Weld Pile Plates	2 hrs	Fri 7/11/14	Fri 7/11/14
10		Install Abut/WW 1	3 hrs	Fri 7/11/14	Sat 7/12/14
11		Post Tensioning Abut 1	2 hrs	Sat 7/12/14	Sat 7/12/14
12		Install Abut/WW 2	3 hrs	Sat 7/12/14	Sat 7/12/14
13		Post Tensioning Abut 2	2 hrs	Sat 7/12/14	Sat 7/12/14
14		Grout Pile Cavities	3 hrs	Sat 7/12/14	Sat 7/12/14
15		Grout Pile Cure Time	12 hrs	Sat 7/12/14	Sat 7/12/14
16		Water Repellent	3 hrs	Sat 7/12/14	Sat 7/12/14
17		Install Bearings	2 hrs	Sat 7/12/14	Sat 7/12/14
18		Granular Backfill	4 hrs	Sat 7/12/14	Sun 7/13/14
19		Type 4 Stone Fill	4 hrs	Sat 7/12/14	Sun 7/13/14
20		Erect Next Beams	5 hrs	Sat 7/12/14	Sun 7/13/14
21		Backfill for Approaches	2 hrs	Sun 7/13/14	Sun 7/13/14
22		Install Approach Slab 1	2 hrs	Sun 7/13/14	Sun 7/13/14
23		Install Approach Slab 2	2 hrs	Sun 7/13/14	Sun 7/13/14
24		Rapid Set Concrete	4 hrs	Sun 7/13/14	Sun 7/13/14
25		Sand Borrow & Subbase	4 hrs	Sun 7/13/14	Sun 7/13/14
26		Rapid Set Concrete Cure Time	12 hrs	Sun 7/13/14	Mon 7/14/14
27		Set Up One Lane Traffic	2 hrs	Mon 7/14/14	Mon 7/14/14
28		Set Barrier on Bridge & Approach	2 hrs	Mon 7/14/14	Mon 7/14/14
29		Re Open Bridge 15	0 days	Mon 7/14/14	Mon 7/14/14

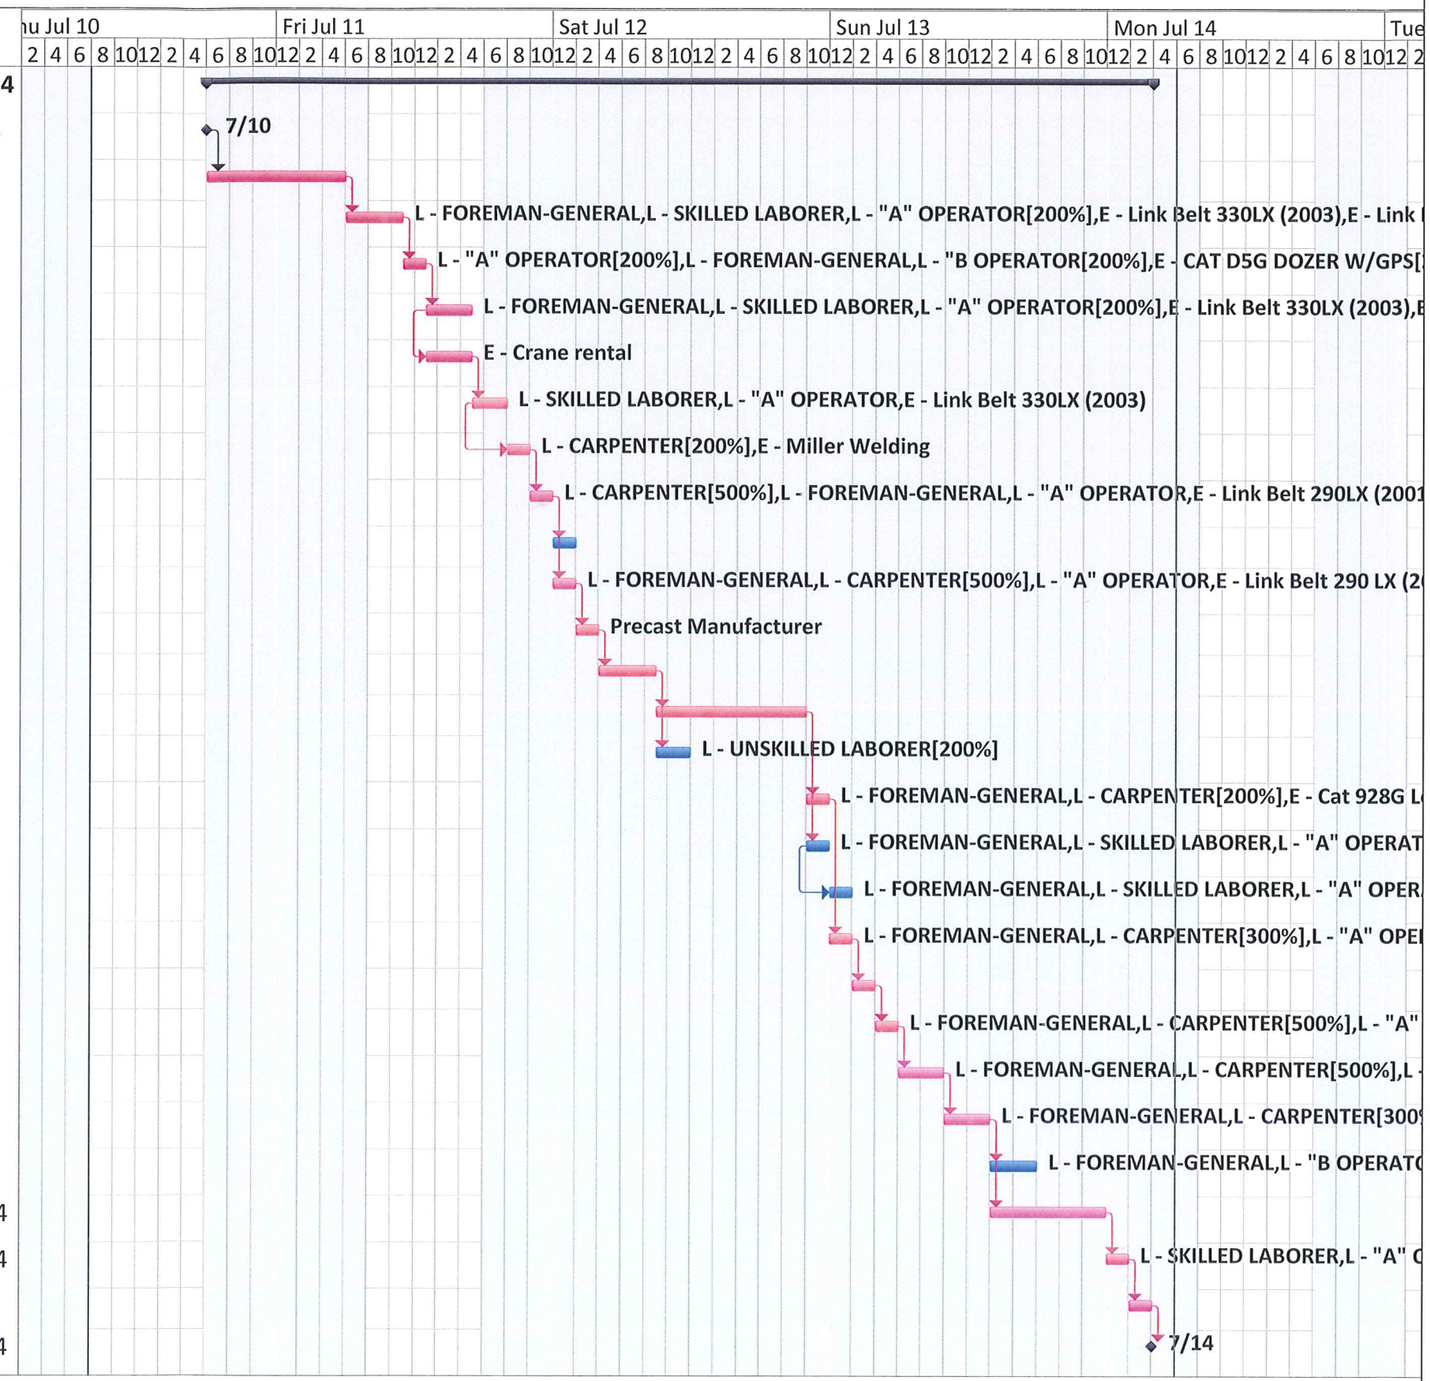

Project: Bridge 15 BCP Hourly
Date: Tue 3/25/14

Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only	
Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Deadline	
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Progress	
