INSTALLATION REPORT

DataMaster DMT: 100148
Location: Berlin PD
Calibration Date: 11/09/2011
Certification Date: 11/14/2011
Installation Date: 12/08/2011
Installed by: STEVEN E HARNOIS

Site meets specification in doc P-ALC-210

Default Options Loaded

Diagnostic Results

```
VERSIONS
DMT: 1.01
PIC: 2.06
Modem: 2.2
Questions: 2.0

TEMPERATURES

Sample Chamber = 48.7°C
Breath Tube    = 48.1°C
Digital Sim    = 34.0°C

SETTINGS
Lamp Voltage   = 1.64 V
Cooler Voltage = 1.69 V
Bias Voltage   = 80 V
Chopper Freq   = 530 Hz

PUMP INFO
Flow Rate = 5.733 L/M

DETECTOR INFO
PUMP     ON        OFF
MAX(V)   -0.0073   -0.0043
MIN(V)   -0.0087   -0.0055

FILTER INFO
Filter 1  -0.005  Zero = true
Filter 2   0.356  Zero = true
Filter 3   0.210  Zero = true

CALIBRATION CHECK
Xq  = 0.084  0.83%
```

Accuracy and Precision Check

Concentration	= 0.101 g/210L
Lot #	= 12-38-100
Range	= 0.096 - 0.106
Average	= 0.100 g/210L
Std Dev	= 0.0000

RF Detection Test

Passed

Sample Acceptance Test

Passed

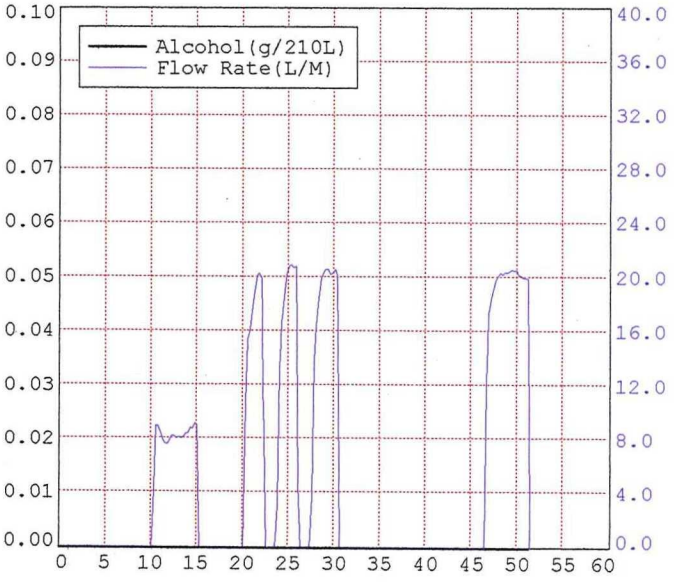

INSTALLATION PASSED

Performed by _____ Date 12/08/2011

Reviewed by _____ Date 12-08-11

SEH 12/08/11
