INSTALLATION REPORT

DataMaster DMT: 100154
Location: Washington County SO
Calibration Date: 11/16/2011
Certification Date: 11/17/2011
Installation Date: 12/08/2011
Installed by: STEVEN E HARNOIS

Site meets specification in doc P-ALC-210

Default Options Loaded

Diagnostic Results

```
VERSIONS
DMT: 1.01
PIC: 2.05
Modem: 2.2
Questions: 2.0

TEMPERATURES

Sample Chamber = 48.7°C
Breath Tube    = 48.1°C
Digital Sim    = 34.0°C

SETTINGS
Lamp Voltage   = 1.72 V
Cooler Voltage = 1.69 V
Bias Voltage   = 81 V
Chopper Freq   = 530 Hz

PUMP INFO
Flow Rate = 5.752 L/M

DETECTOR INFO
PUMP     ON        OFF
MAX(V)   0.1427    0.1407
MIN(V)   0.1370    0.1388

FILTER INFO
Filter 1   0.140   Zero = true
Filter 2   0.475   Zero = true
Filter 3   1.471   Zero = true

CALIBRATION CHECK
Xq  = 0.087  0.10%
```

Accuracy and Precision Check

Concentration = 0.101 g/210L
Lot # = 12-38-100
Range = 0.096 - 0.106
Average = 0.099 g/210L
Std Dev = 0.0000

RF Detection Test

Passed

Sample Acceptance Test

Passed

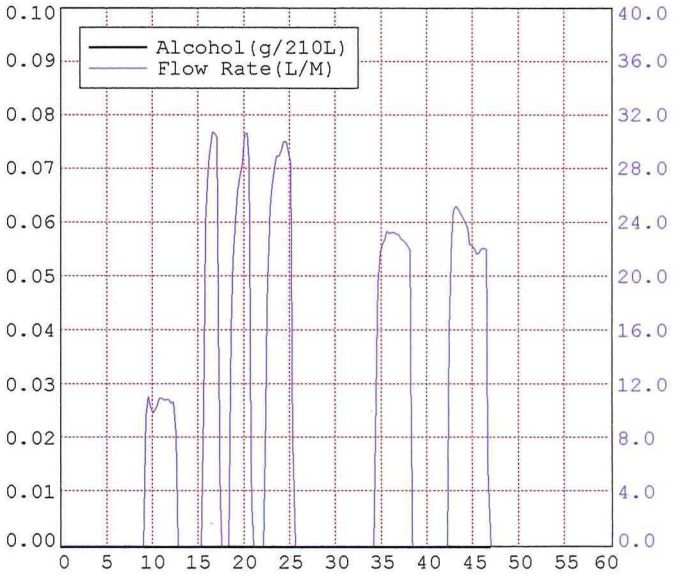

INSTALLATION PASSED

Performed by _____ Date 12/08/2011

Reviewed by _____ Date 12-08-11

Steve 12/08/11
