INSTALLATION REPORT

DataMaster DMT: 100163
Location: Bennington County SO
Calibration Date: 09/14/2011
Certification Date: 09/15/2011
Installation Date: 04/10/2012
Installed by: AMANDA BOLDUC

Site meets specification in doc P-ALC-210

Default Options Loaded

Diagnostic Results

```
VERSIONS
DMT: 1.01
PIC: 2.06
Modem: 2.2
Questions: 2.0

TEMPERATURES

Sample Chamber = 49.1°C
Breath Tube    = 42.8°C
Digital Sim    = 34.0°C

SETTINGS
Lamp Voltage   = 1.80 V
Cooler Voltage = 1.57 V
Bias Voltage   = 80 V
Chopper Freq   = 546 Hz

PUMP INFO
Flow Rate = 4.875 L/M

DETECTOR INFO
PUMP     ON        OFF
MAX(V)   -0.2443   -0.2427
MIN(V)   -0.2496   -0.2439

FILTER INFO
Filter 1  -0.243  Zero = true
Filter 2  -0.028  Zero = true
Filter 3   0.318  Zero = true

CALIBRATION CHECK
Xq  = 0.077  0.67%
```

Accuracy and Precision Check

Concentration	= 0.101 g/210L
Lot #	= 12-64-100
Range	= 0.096 - 0.106
Average	= 0.103 g/210L
Std Dev	= 0.0000

RF Detection Test

Passed

Sample Acceptance Test

Passed

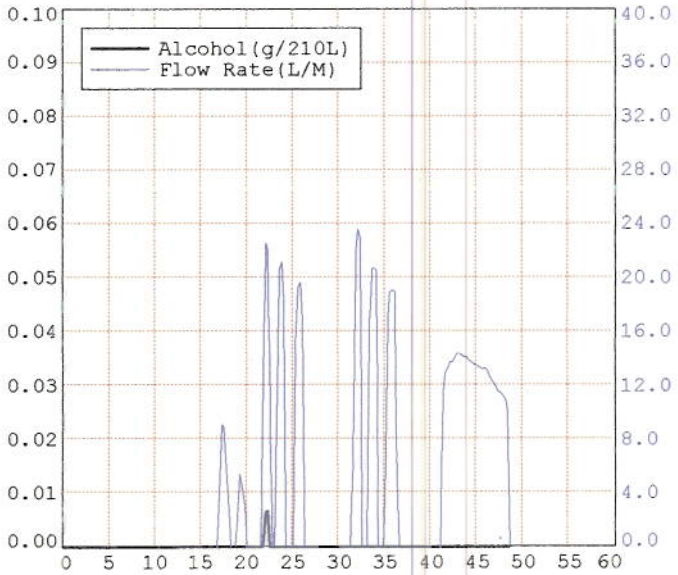

INSTALLATION PASSED

Performed by Amanda Bolduc Date 04/10/2012

Reviewed by Date 4/11/2012
