INSTALLATION REPORT

DataMaster DMT: 123006
Location: ROYALTON PD
Calibration Date: 05/18/2012
Certification Date: 05/18/2012
Installation Date: 07/20/2016
Installed by: ROBERT DRISCOLL

Default Options Loaded

Diagnostic Results

```
VERSIONS
DMT: 2.00
PIC: 2.05
Modem: 2.6
Questions: 2.1

TEMPERATURES

Sample Chamber = 48.9°C
Breath Tube    = 47.3°C
Digital Sim    = 34.0°C

SETTINGS
Lamp Voltage   = 1.77 V
Cooler Voltage = 1.69 V
Bias Voltage   = 80 V
Chopper Freq   = 537 Hz

PUMP INFO
Flow Rate = 4.963 L/M

DETECTOR INFO
PUMP     ON        OFF
MAX(V)   0.5134    0.5173
MIN(V)   0.5112    0.5161

FILTER INFO
Filter 1   0.517  Zero = true
Filter 2   0.937  Zero = true
Filter 3   1.576  Zero = true

CALIBRATION CHECK
Xq  = 0.118  0.38%
```

Accuracy and Precision Check

Concentration = 0.099 g/210L
Lot # = 16-05-100
Range = 0.094 - 0.104
Average = 0.100 g/210L
Std Dev = 0.0004

RF Detection Test

Passed

Sample Acceptance Test

Passed

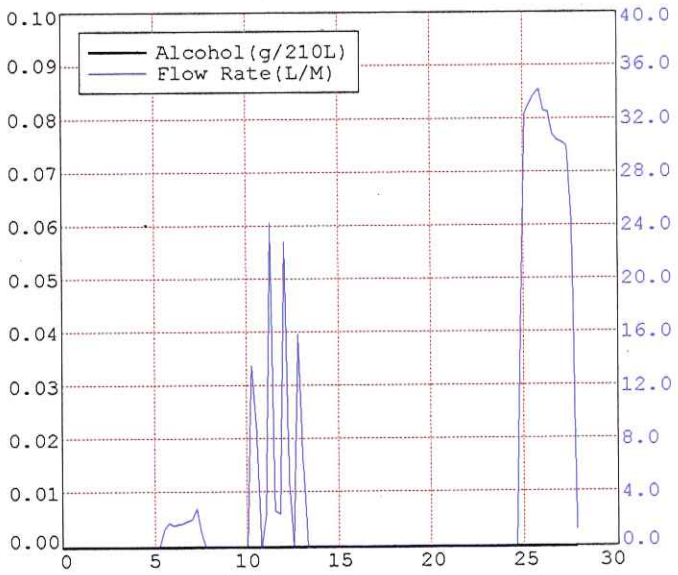

INSTALLATION PASSED

NIST Thermometer s/N 111814362 34.1°C
RCD 7/20/16

Performed by RCD Date 07/20/2016

Reviewed by Date 7/27/16

VERMONT FORENSIC LABORATORY

PO BOX 47
WATERBURY, VERMONT 05676-0047
TEL: 802-244-8788
FAX: 802-241-5557
http://vfl.vermont.gov

DataMaster DMT Site Evaluation Checklist

Agency or Site Information

Name: Royalton PD

Address: 2460 RT 14 PO Box 44
South Royalton, VT 05068

Phone: (802) 763-7776

Fax: (802) 763-7711

Personnel Information

Head of Site: Robert L Hull

Current DataMaster Supervisor (s):

John Breault

Proposed DataMaster Supervisor(s):

(Proposed) DataMaster DMT Environment

Limited Controlled Access:	Y	N
Low Activity Area:	Y	N
Unlimited Access by Other Law Enforcement Personnel	Y	N
Access by VFL Technical Services	Y	N
Air Conditioned	Y	N
Room Temperature 65° - 85° F	Y	N
Adequate Ventilation	Y	N
Free of Cleaning Supplies	Y	N
Clean	Y	N

(Proposed) DataMaster DMT Connection(s)

Power: Min 15 Amp	Y	N
Limited low power sharing:	Y	N
Ethernet Available:	Y	N

Distance to Ethernet 4'

(Proposed) DataMaster DMT Site Maintenance Agreement

Will notify VFL Alcohol Program staff of maintenance and supply needs promptly:	Y	N
Will notify VFL Alcohol Program staff of changes in building conditions or moves promptly:	Y	N
Will notify VFL Alcohol Program staff of relevant personnel changes at site promptly:	Y	N

	Print Name	Signature	Date
VFL Representative:	Robert Driscoll	[illegible]	4/14/16
Agency Representative:	Robert L. Hull	Robert L Hull	4/14/16
