














































































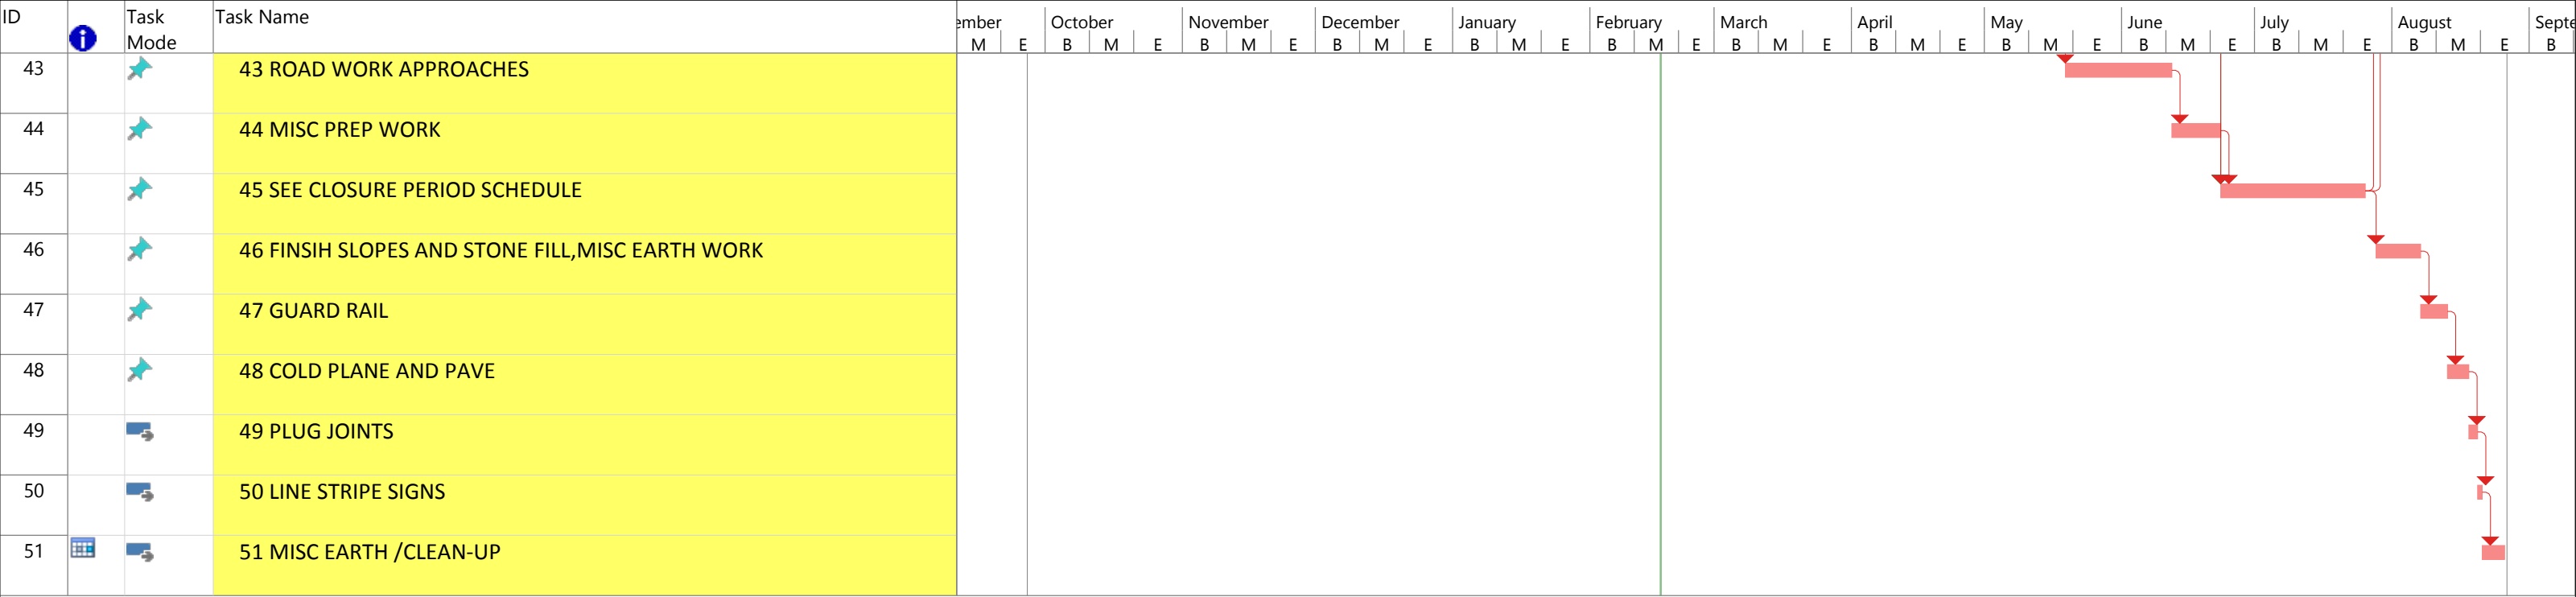


Project: cavendish scheduele no Date: Mon 2/17/14	Task		Inactive Milestone		Start-only		Critical Split	
	Split		Inactive Summary		Finish-only		Path Driving Predecessor Milestone Task	
	Milestone		Manual Task		External Tasks		Path Driving Predecessor Summary Task	
	Summary		Duration-only		External Milestone		Path Driving Predecessor Normal Task	
	Project Summary		Manual Summary Rollup		Deadline		Progress	
	Inactive Task		Manual Summary		Critical		Manual Progress	

ID		Task Mode	Task Name	ember	E	October	November	December	January	February	March	April	May	June	July	August	Sept
				M		B	M	E	B	M	E	B	M	E	B	M	E
22			22 SELF PERFORMANCE CVEP														
23			23 SELF PERFORMACE DVEP/REVIEW														
24			24 CONSTRUCT CASTING BED/ENCLOSURE														
25			25 HOLDAY SHUT DOWN														
26			26 POUR 1, RBAR,FORM,POUR														
27			27 CURE POUR # 1														
28			28 POUR 2, RBAR,FORM,POUR														
29			29 CURE POUR #2														
30			30 APPROACH SLABS A,B,C,D														
31			31 CURE APPROACH SLABS A,B,C,D														
32			32 APPROACH SLABS E,F,G,H														
33			33 CURE APPROACH SLABS E,F,G,H														
34			34 CONSTRUCT RAIL SYSTEM FOR HORIZONTAL SLIDE PBU/PARTIAL														
35			35 STRUCT. STEEL DELIVERY-SET														
36			36 FORM PBU 1,2,														
37			37 R-BAR PBU #1&#2														
38			38 FORM PBU #3&#4														
39			39 R-BAR PBU #3&#4														
40			40 CAST PBU 1,2,3,4														
41			41 CURE PBU														
42			42 INSTALL SIGNS AND DETOR														

Project: cavendish schedule no  
Date: Mon 2/17/14

Task		Inactive Milestone		Start-only		Critical Split	
Split		Inactive Summary		Finish-only		Path Driving Predecessor Milestone Task	
Milestone		Manual Task		External Tasks		Path Driving Predecessor Summary Task	
Summary		Duration-only		External Milestone		Path Driving Predecessor Normal Task	
Project Summary		Manual Summary Rollup		Deadline		Progress	
Inactive Task		Manual Summary		Critical		Manual Progress	



Project: cavendish scheduele no  
Date: Mon 2/17/14

Task


Split


Milestone


Summary


Project Summary


Inactive Task











Inactive Milestone


Inactive Summary


Manual Task


Duration-only


Manual Summary Rollup


Manual Summary











Start-only


Finish-only


External Tasks


External Milestone


Deadline


Critical














Critical Split

Path Driving Predecessor Milestone Task

Path Driving Predecessor Summary Task

Path Driving Predecessor Normal Task

Progress

Manual Progress

